

24



NAVARRO COUNTY ROAD AND BRIDGE DEPARTMENT

NAVARRO COUNTY COURTHOUSE

300 W. 3<sup>RD</sup> AVE.

CORSICANA, TEXAS 75110

APPROVAL FORM FOR UTILITY EASEMENTS

Date: 02/27/2026

Applicant: Valor Telecom Texas, LLC

Address: 4005 N Rodney Parham Rd, Little Rock, AR 72212

Phone #: 501-748-7807

Type of utility construction requested: (pipeline and product, cable and type, utility and type:

Fiber Optic Placement

Name of Utility Company: Valor Telecom Texas, LLC

Location of Utility Construction: (location map must be attached) (see attached map)

16122 NW 3120

Attach location map or drawing, description of proposed utility line and appurtenances fully shown with distance of utility lines being replaced or installed in relationship with County Roads. Show on map or drawing the location of any road bore, length of bore and size of encasement that the utility line will be passing through.

Estimated start date of construction: 12/31/2025

Estimated completion date of construction: 02/17/2026 ( 60 days pending approval )

County of Navarro

Specifications for placing utilities within Navarro County Right-Of-Way

1. In the event it becomes necessary to alter or relocated the utility for which permission is sought, due to widening or improving the county road within the existing road easement at the point or along the route of said utility construction, applicant or its successor, if any, will perform the alteration or relocation at its own cost and expense, and said company will save and hold harmless Navarro County from any claims, or causes of action due to any claims for damages or injuries sustained by any person or property occasioned by its operation under this permit.
2. All road crossings will be bored unless a variance is granted.
3. All road crossings will at a minimum depth of 60" below the lowest existing grade.
4. All parallel utility construction will be a minimum depth of 60" below existing road grade.
5. All right-of-way disturbed by the utility construction will be restored daily to a condition that is as good or better than before construction.
6. In the event construction is delayed or halted by adverse weather conditions, labor stoppages or mechanical difficulties, the company will insure that all ditches are cleaned and will drain as good or better than before construction.
7. The County Commissioner of said Precinct may require the applicant to file a bond for road repairs and damage repairs in the amount the Commissioner determines to cover damage costs for said job. Upon completion of construction at a road crossing or parallel construction in the Right-of-way, contractor will notify the Commissioner so an inspection can be made.
8. A route map of any proposed pipeline together with cross sections shall be submitted with the application. All road crossings shall be located with GPS coordinates.
9. The applicant in consideration of the approval of this request by the Navarro County Commissioners Court does hereby agree, upon completion of the placement of the utilities as set forth in this request, to return the county road, its right-of-way and any improvements or additions to a condition which, in the opinion of the County Commissioner , equals or exceeds the condition in which said county road or right-of-way prior to the time construction started.
10. The applicant shall indemnify, defend, and hold Navarro County harmless from any obligation or claim for damages that may be alleged or any costs or expenses, including but not limited to, reasonable attorneys' fees arising from the applicant's emplacement of the object in the right-of-way which Navarro County may incur, or any claims Navarro County may be legally required to pay resulting from damages caused by the installation contemplated by this agreement. The applicant shall indemnify, defend, and hold Navarro County harmless at any future date for accidental damages to the above ground and/or buried utilities by road working equipment such as motor graders, posthole diggers, shredders, brush cutters, drainage ditch clearing equipment, etc. In the event such damages should occur, the applicant will be notified immediately.

The undersigned agrees that he has read and will abide by all requirements set forth in this form.

Signature of Applicant: Gabrielle Johnson

Date: 02/27/2026

NAVARRO COUNTY

By: [Signature]  
County Judge

Date: 3-9-26

By: [Signature]  
Commissioner of Precinct 4

Date: 3/9/26


## VICINITY MAP

### WINDSTREAM LOCATION MAP

#### WINDSTREAM LOCATION MAP\_NAVARRO COUNTY PERMIT

WINDSTREAM PROPOSES TO INSTALL 21,369' FOC WITHIN ROW  
 540' OF 12 FOC BY DIRECT BORE, 1,358' OF 12 FOC BY DIRECTIONAL BORE,  
 9,667' OF 12 FOC BY DIRECT BURY/PLOWING, 300' OF 24 FOC BY DIRECT BORE,  
 367' OF 24 FOC BY DIRECTIONAL BORE, 2,954' OF 24 FOC BY DIRECT BURY/PLOWING,  
 80' OF 48 FOC BY DIRECT BORE, 1,577' OF 48 FOC BY DIRECT BURY/PLOWING,  
 50' OF 144 FOC BY DIRECT BORE, 300' OF 144 FOC BY DIRECTIONAL BORE,  
 4,176' OF 144 FOC BY DIRECT BURY/PLOWING METHOD.

NO.OF 10" PED-(19),NO.OF 8" PED-(43) & NO.OF 6" PED-(3).

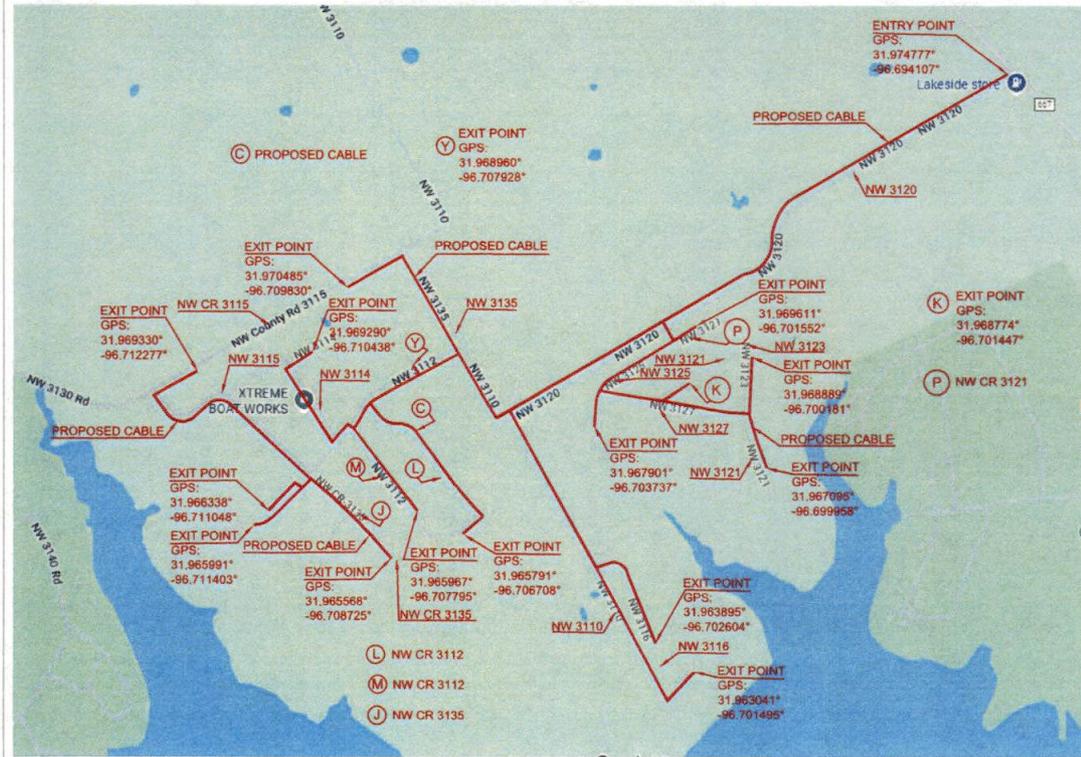

#### Windstream Proposes Fiber Optic Placement:

##### Footage Inside Row:

Method	12 FOC	24 FOC	48 FOC	144 FOC
Buried				
Direct Bore	540'	300'	80'	50'
Directional bore	1,358'	367'		300'
Direct Bury/Plowing	9,667'	2,954'	1,577'	4,176'
Dry Bore				
Total	11,565'	3,621'	1,657'	4,526'
Aerial	12 FOC	24 FOC	48 FOC	144 FOC
Lash To Existing				
10M				
Total				

Total Footage Inside Row: 21,369'

Total Proposed Footage: 21,369'

**⚠️ DIG ALERT: 811,KNOW WHAT'S BELOW,PLEASE CALL BEFORE YOU DIG**

FOR THE PURPOSE OF PROVIDING FIBER OPTIC CABLE FOR INTERNET ACCESS

UG FOOTAGE DETAILS	
DESCRIPTION	FOOTAGE
BORE IN 1.25" CONDUIT	2,995' L.F
TRENCH	0' L.F
DIRECT BURY/PLOWING	18,374' L.F
DRY BORE	0' L.F
<b>TOTAL</b>	<b>21,369' L.F</b>

STRUCTURE DETAILS	
6" PED	3 E.A
8" PED	43 E.A
10" PED	19 E.A
AERIAL TERMINAL	0 E.A

AERIAL FOOTAGE DETAILS	
NEW 10M STRAND	0' L.F
ELASHING	0' L.F
NO LASHING	0' L.F
<b>TOTAL</b>	<b>0' L.F</b>

DATE CREATED: 12/29/2025

DATE REVISD:

DRAWN BY: CYIENT INC

COMPANY: WINDSTREAM

SYSTEM: DAWSON\_TX

PROJECT NUMBER: 740053764

DESCRIPTION:  
SEFH12962  
1EA1\_SERVING\_AREA

MAP: VICINITY MAP

CYIENT INC
